

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2022					Half 1, 2023					Half 2, 2023					Half 1, 2023			
							J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J
1		<b>CONSTRUCTION PERIOD</b>	<b>356.5 days</b>	<b>Mon 8/1/22</b>	<b>Fri 12/22/23</b>																				
2		START OF PROJECT	0 days	Mon 8/1/22	Mon 8/1/22																				
3		END OF PROJECT	0 days	Fri 12/22/23	Fri 12/22/23	82,454,507,63,54																			
4		<b>SITE</b>	<b>193.5 days</b>	<b>Mon 8/1/22</b>	<b>Mon 5/1/23</b>																				
5		COMMENCE CONS	1 day	Mon 8/1/22	Mon 8/1/22																				
6		MOBILIZE AND SAF	2 days	Mon 8/1/22	Tue 8/2/22	5SS,2																			
7		STRIP, GRUB AND	2 days	Wed 8/3/22	Thu 8/4/22	6SS																			
8		POWER & TECHNIC	1 day	Fri 8/5/22	Mon 8/8/22	7																			
9		SURVEY AND STAK	3 days	Mon 8/8/22	Thu 8/11/22	8																			
10		OVER-EX PAD, OVE	2 days	Thu 8/11/22	Mon 8/15/22	9																			
11		FENCE SITE & STAG	2 days	Mon 8/15/22	Wed 8/17/22	10																			
12		ROUGH GRADE SIT	4 days	Wed 8/17/22	Tue 8/23/22	11																			
13		S W W P & PROTEC	3 days	Tue 8/23/22	Fri 8/26/22	12																			
14		ALL SANITARY SEW	20 days	Fri 8/26/22	Fri 9/23/22	13																			
15		STAKE TRENCHES	3 days	Fri 9/23/22	Wed 9/28/22	14																			
16		LIMETREAT BUILDI	3 days	Wed 9/28/22	Mon 10/3/22	15																			
17		COMPACT/GRADE	1 day	Mon 10/3/22	Tue 10/4/22	16																			
18		FIRE LINES AND DC	15 days	Tue 10/4/22	Tue 10/25/22	17																			
19		CERTIFY PAD	1 day	Tue 10/25/22	Wed 10/26/22	18																			
20		INSTALL FIRE RISER	1 day	Fri 10/28/22	Mon 10/31/22	19FS+16 hrs																			
21		FINISH GRADE/LIM	2 days	Mon 10/31/22	Wed 11/2/22	20																			
22		STAKE FOR CURBS	4 days	Wed 11/2/22	Tue 11/8/22	21																			
23		CURB AND GUTTER	15 days	Wed 11/9/22	Wed 11/30/22	22FS+8 hrs																			
24		ALL ROUGH SITE LI	10 days	Wed 11/16/22	Wed 11/30/22	23FF																			
25		INSTALL MAIN LINE	8 days	Fri 11/18/22	Wed 11/30/22	24FF																			
26		MAIN POWER / PH	10 days	Tue 11/15/22	Tue 11/29/22	25FS-88 hrs																			
27		IRRIGATION SLEEVI	1 day	Fri 11/25/22	Mon 11/28/22	26FS-16 hrs																			
28		BASE ROCK	4 days	Mon 11/28/22	Fri 12/2/22	27																			
29		GASLINE SLEEVING	1 day	Fri 12/2/22	Mon 12/5/22	28																			
30		INSTALL HEADERS	1 day	Mon 12/5/22	Tue 12/6/22	29																			
31		LIGHT POLE BASES	4 days	Tue 12/6/22	Mon 12/12/22	30																			
32		ASPHALT PAVEMEN	1 day	Mon 12/12/22	Tue 12/13/22	31																			
33		SITWORK PAVEMI	4 days	Tue 12/13/22	Mon 12/19/22	32																			
34		TRASH ENCLOSURE	4 days	Tue 12/13/22	Mon 12/19/22	33FF																			
35		CMU TRASH ENCLC	4 days	Mon 12/19/22	Fri 12/23/22	34																			
36		TRASH ENCLOSURE	4 days	Mon 12/19/22	Fri 12/23/22	35FF																			
37		ENTRY PAVEMENT	10 days	Fri 12/23/22	Fri 1/6/23	36																			
38		TRANSFORMER AN	2 days	Fri 1/6/23	Tue 1/10/23	37																			
39		PG&E GAS MANIFC	2 days	Tue 1/10/23	Thu 1/12/23	38																			
40		IRRIGATION SYSTE	10 days	Thu 1/12/23	Fri 1/27/23	39																			

Project: Cambria Hotel and Suit Date: Fri 3/4/22	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			


























ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2022							Half 1, 2023							Half 2, 2023							Half 1, 2024
							J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J			
533		CLOSE OUT BUILDING	0 days	Tue 6/27/23	Tue 6/27/23	532																						
534		FIRE DEPARTMENT CITY	1 day	Tue 6/27/23	Wed 6/28/23	533																						
535		COUNTY OF SAN JUAN	1 day	Wed 6/28/23	Thu 6/29/23	534																						
536		CITY PUBLIC WORKS	1 day	Fri 6/30/23	Mon 7/3/23	536																						
537		HEALTH DEPARTMENT	1 day	Mon 7/3/23	Wed 7/5/23	537																						
538		TEMP CERTIFICATE	1 day	Wed 7/5/23	Thu 7/6/23	538																						
540		PUNCH LIST	4 days	Thu 7/6/23	Wed 7/12/23	539																						
541		CONTRACTORS FLORIDA	25 days	Wed 7/12/23	Wed 8/16/23	540																						
542		CERTIFICATE OF OCCUPANCY	0 days	Wed 8/16/23	Wed 8/16/23	541																						
543		TRAINING AND ASSESSMENT	1 day	Wed 8/16/23	Thu 8/17/23	542																						
544		CLOSE OUT PARTY	0 days	Thu 8/17/23	Thu 8/17/23	543																						

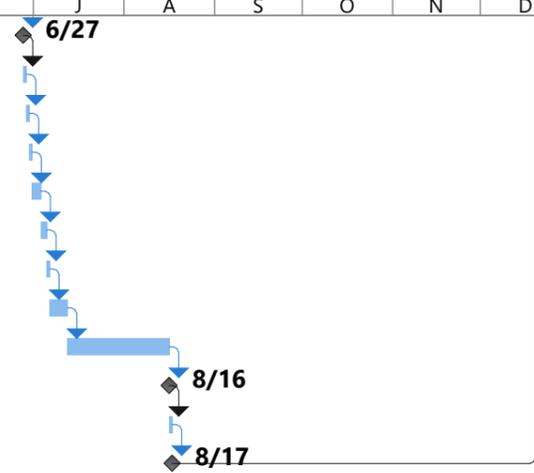

Project: Cambria Hotel and Suit Date: Fri 3/4/22	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
